TULSA DISTRICT, USACE ACQUISITION & MILITARY PROGRAM REVIEW 20 FEBRUARY 2019

MICHELLE LAY PATRICK BEARD 20 February 2019

> eragency and 0 D





"The views, opinions and findings contained in this report are those of the authors(s) and should not be construed as an official Department of the Army position, policy or decision, unless so designated by other official documentation."













District Acquisition







BORDER INFRASTRUCTURE HORIZONTAL AE

PROJECT INFORMATION

- Project Title: Horizontal AE Services for BI Program
- Description / Scope: Nationwide horizontal design services in support of DHS programs.
- Contract Capacity: \$720M across up to 24 IDCs
- Acquisition Strategy: 6 solicitations: UR, SB, 8(a), SDVOSB, WOSB, and HZ

NALL FOTONIEC

• PM: Michelle Lay

	1	2	3	4	5
Set Aside	Unrestricted	Small Business	8(a)	SDVOSB	WOSB/HZ
# of Contracts	4	6	З	3	8
Minimum Guarantee	\$2,500	\$2,500	\$2,500	\$2,500	\$2,500
Maximum Task Orde	\$20,000,000	\$5,000,000	\$3,000,000	\$3,000,000	\$1,000,000
Total Shared Capaci	\$245,000,000	\$245,000,000	\$65,000,000	\$65,000,000	\$100,000,000

Total Capacity: \$720,000,000

Percent of Capacity set aside for Small Businesses: 65.97%

Scheduled	Key Action	Actual
10/24/18	Acq Strat/Plan District Approval	10/26/18
2/22/19	PARC Acq Strat/Plan Approval	
2/26/19	Advertise 1st Synopsis (Unrestricted)	
3/26/19	Receive SF330s from UR Firms	
4/23/19	UR AE Board Complete	
4/26/19	UR AE Board Report Approved by CMDR	
5/2/19	Issue UR RFP	
5/12/19	Receive UR Proposals	
6/6/19	UR Negotiations Complete	
6/22/19	Unrestricted AE contract award(s)	

STATUS/CHALLENGES/WAY AHEAD

Status:

- > Submitted revised Acquisition Strat/Plan and Consolidation D&Fs for PARC Approval
- > UR synopsis drafted
- Seeking Peer Review Waiver
- > P2 schedule updated based on current projected dates

Challenges:

None

Way Ahead:

- Receive acquisition document approval
- Finalize staffing for AE Selection Board







AE GENERAL SERVICES

PROJECT INFORMATION

- Project Title: General Services Architect Engineer IDCs
- Description / Scope: AE contracts for design services in support of all SWT mission areas
- Contract Capacity: \$99M across up to 9 IDCs
- Acquisition Strategy: 1 solicitation with reserves: UR, SB, WOSB, SDVOSB

MILESTONES

• PM: Michelle Lay

Pool No.	Synopsis Description	Reserved Capacity	Contract Type	Description	Task Order Range	Min Guarantee
1	General Services	\$75M	UR Pool, Multiple award A-E contract, fixed firm price (FFP) task orders (TOS), 5 firms	Multi- Discipline A-E IDCs, 5 years (3 year base, 2-year option)	\$2M - \$10M	\$2.5K
2	General Services	\$12M	SB Pool, Multiple award A-E contract, FFP TOs, up to 2 firms	Multi- Discipline A-E IDCs, 7 years (3 year base, 2-year option)	<\$2M	\$2.5K
3	General Services	\$6M	WOSB, Single award A-E contract, FFP TOs, up to 1 firms	Multi- Discipline A-E IDC, 5 years (3 year base, 2-year option)	<\$2M	\$2.5K
4	General Services	\$6M	SDVOSB, Single award A-E contract, FFP TOs, up to 1 firms	Multi- Discipline A-E IDC, 5 years (3 year base, 2-year option)	<\$2M	\$2.5K
	TOTAL		Unrestricted= SBSA=	\$75M (75.8%) \$24M (24.2%)		

Scheduled	Key Action	Actual
2/22/19	Acq Strat/Plan District Approval	
3/8/19	PARC Acq Strat/Plan Approval	
3/11/19	Advertise Synopsis	
4/11/19	Receive SF330s	
5/15/19	AE Board Complete	
5/16/19	AE Board Report Approved by CMDR	
5/22/19	Issue RFP	
6/3/19	Receive Proposals	
6/19/19	Negotiations Complete	
7/3/19	AE contract award(s)	

STATUS/CHALLENGES/WAY AHEAD

Status:

Acquisition documents routing for review

Challenges:

None

Way Ahead:

- Submit acquisition documents to PARC
- Prepare synopsis
- > Respond to PARC comments and receive acquisition document approval
- ➢ Finalize staffing for AE Selection Board







DISTRICT ACQUISITION UPDATE

Other major acquisitions planned

- Hydropower MATOC Approx \$35M Construction MATOC primarily for crane rehab/replacement for the Hydropower Program within SWD; Planned issue Phase 1 October 2019 with target award by June 2020
- Civil Works MATOC Acquisition will kick off in FY20
- AE Survey Planned solicitation for replacement survey IDC in FY19 with target award summer 2020
- AE Real Estate Planned nationwide contract for support to the Air Force; planned solicitation in FY19 with target award 2nd quarter 2020
- AE Geotechnical Planned solicitation for replacement IDC in FY20





District MILCON







FY19 ERCIP-FT SILL

PROJECT INFORMATION

- Project Title and Location: Install Substation Interconnection
- Project Number/P2#: PN092569 / 471129
- Description / Scope: Design and construct a substation interconnection to provide electrical resiliency for critical missions IAW Army Directive 2017-07.
- KTR: SWT/AE
- PA: \$7-12M
- Contract Amount: TBD
- Acquisition Strategy: DB, Firm Fixed Price
- Estimated Construction Completion (Physical Comp): TBD
- PM: Gary Holt
- ERCIP DoD Energy Resilience Conservation Investment Pgm

MILESTONES

Scheduled	Key Action	Actual
MAY 2019	Ready to Advertise (RTA)	
JUN 2019	Advertise	
AUG 2019	Award	



STATUS/CHALLENGES/WAY AHEAD

Status:

- ➤Working RFP Development
- Trench/bore and install new underground conduit and electrical lines from feeders 1-4 and 8 of the Sheridan Road electrical sub-station to the Moway Road substation. Repair existing feeders, poles, conductors, switches and all other related materials at existing sub-station as necessary.







FY20 MILCON-FT SILL

PROJECT INFORMATION

- Project Title and Location: Adv Individual Training Barracks Cplx, Ph2
- Project Number/P2#: PN075953 / 393481
- Description / Scope: Design and Construct Reception Barracks complex to facilitate the basic training requirements
- KTR: In-House: NWK (DFAC) & SWT (Barracks)
- PA: \$70-76M
- Contract Amount: TBD
- Acquisition Strategy: DBB, Firm Fixed Price
- Estimated Construction Completion (Physical Comp): TBD
- DM: Ron Rosebrook
- PM: Gary Holt

MILESTONES

Scheduled	Key Action	Actual
30 SEP 2019	Ready to Advertise (RTA)	
OCT / NOV 2019	Advertise	
DEC / Jan 2019	Award	



STATUS/CHALLENGES/WAY AHEAD

Status:

There will be 2 separate projects

- This phase completes construction of a standard design, battalion sized, Advanced Individual Trainee (AIT) Complex. Primary facilities are two barracks/company operations (BCOF's) for 600 soldiers and one Dining Facility (1300 person)
- Barracks Portion will advertise DBB Unrestricted 183,000 SF Barracks and Company operations (\$50-60M)
- Dinning Facility will Advertise Based on sources sought response (\$9-14M), to construct a 1300 person DFAC








MCAAP

PROJECT INFORMATION

- Project Title and Location: FY19 Replace Bulk Diesel System
- Project Number/P2#: DESC18S2 / 464947
- Description / Scope: Design and construct Replacement of Bulk Diesel System
- Designer: Omaha District
- PA: \$5-8M
- Contract Amount: TBD
- Acquisition Strategy: D-B-B, Best Value
- Estimated Construction Completion (Physical Comp): Sept 2020
- **PM:** CPT Garrett D. Anderson

	MILESTONES		
Scheduled	Key Action	Actual	<u>S</u> 1
JUL 2019	Ready to Advertise (RTA)		
AUG 2019	Advertise		
SEP 2019	Award		

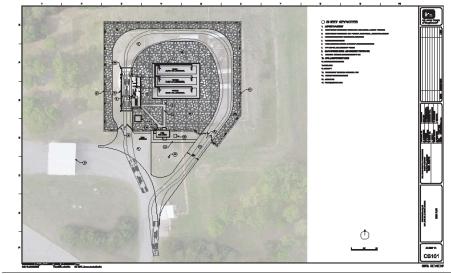

STATUS/CHALLENGES/WAY AHEAD

<u>Status</u>:

 Project is currently in the design Phase
 Will Construct 3 tanks with a total storage capacity of 150,000 Gal, Truck off-loading facility, pumps, filters and associated piping. Project will also include containment and storm water management systems with a canopy.







MCAAP

PROJECT INFORMATION

- Project Title and Location: FY21 Ammunition Reclamation Center
- Project Number/P2#: PN65443 / 455778
- Description / Scope: Design and Construct Ammunition Reclamation Center
- KTR: TBD
- PA: \$30-40M
- Contract Amount: TBD
- Acquisition Strategy: DBB, MATOC
- Estimated Construction Completion (Physical Comp): TBD
- PM: CPT Garrett D. Anderson



STATUS/CHALLENGES/WAY AHEAD

Status:

- Project is currently in the design phase
- Construct a 40,000 AF Ammunition Demil Facility, Project includes demilitarization process facilities, unattended process control rooms, employee change rooms, break room, and rail access.







ScheduledKey ActionActualDEC 2020Ready to Advertise (RTA)JAN 2021AdvertiseMAR 2021AwardImage: State of the state of th

MILESTONES

PROJECT INFORMATION

- Project Title and Location: FY18 Improve Liberator Gate
- Project Number/P2#: WWYK173005/454813
- Description / Scope: Design and construct ATFP compliant entry control point
- **Designer:** Blair-Remy
- PA: \$1.5-3M
- Contract Amount: TBD
- Acquisition Strategy: D-B-B
- Estimated Construction Completion (Physical Comp): Oct 2019

MILESTONES

• PM: Ruben Del Rio

Contraction of the second	
N	CALIFIC DE CALIFIC
RE	

(Current/Existing)

STATUS/CHALLENGES/WAY AHEAD

<u>Status:</u>

Actual

- Design Phase underway
- Construct a steel frame reinforced masonry unit traffic check house structure to replace facility 3604. Provide a steel frame canopy structure across two in-bound and two out-bound lanes. Add one additional out-bound traffic lane and reconstruct traffic weave features to accommodate the additional lane width.





US Army Corps of Engineers ®

ScheduledKey ActionMAY 2019Ready to Advertise (RTA)JUN 2019Advertise

JUN 2019	Advertise	
SEP 2019	Award	

11

PROJECT INFORMATION

- Project Title and Location: FY19 Commercial Vehicle Inspection Facility
- Project Number/P2#: WWYK153007/133265
- Description / Scope: Design and construct ATFP compliant Commercial Vehicles Access Control Point (ACP)
- Designer: TBD
- PA: \$10-15M
- Contract Amount: TBD
- Acquisition Strategy: Design-Bid-Build (DBB)
- Estimated Construction Completion (Physical Comp): TBD
- PM: Ruben Del Rio

MILESTONES

Scheduled	Key Action	Actual
NOV 2019	Ready to Advertise (RTA)	
NOV 2019	Advertise	
MAR 2020	Award	



STATUS/CHALLENGES/WAY AHEAD

<u>Status:</u>

Project Design Currently Underway

➤Construction includes a security control center, an inspection station, gates, inbound roadways, large vehicle staging, reject/denial road turnouts, final denial barrier systems, final over-watch facility and outbound roads, including traffic calming and control features, to base road network.







PROJECT INFORMATION

- Project Title and Location: 10th Flight Test Squadron Operations Facility
- Project Number/P2#: WWYK199000/ 475976
- Description / Scope: Design and construct ATFP compliant operations facility
- Designer: TBD
- PA: \$4.5-7.5M
- Contract Amount: TBD
- Acquisition Strategy: Design-Bid-Build (DBB)
- Estimated Construction Completion (Physical Comp): TBD
- PM: Ruben Del Rio



(Current/Existing)

STATUS/CHALLENGES/WAY AHEAD

MILESTONES

Scheduled	Key Action	Actual
AUG 2019	Ready to Advertise (RTA)	
NOV 2019	Advertise	
FEB 2020	Award	

<u>Status</u>:

➤Design is underway

➤Construct a 1,358 SM permanent facility to house the 10th Flight Test Squadron, Tinker AFB. The facility will be constructed of masonry veneer, steel frame structure, reinforced concrete foundation and floors, roof, fire protection, HVAC systems, utilities, and other support as required to provide a complete and usable The facility








13

PROJECT INFORMATION

- Project Title and Location: FY19 B9201 Program Office (Ph 1)
- Project Number/P2#: P2# 468463
- Description / Scope: DBB Design of B9201 interior renovation and up-fit for aircraft Program Office (approx. 60,000 sqft)
- A/E: Burns & McDonnell
- PA/CWE: \$35-45M
- Contract Amount: TBD
- Acquisition Strategy: Unrestricted
- Estimated Construction Completion (Physical Comp): Apr 2021
- BOD: Jul 2021
- PM: Jeremy Smith

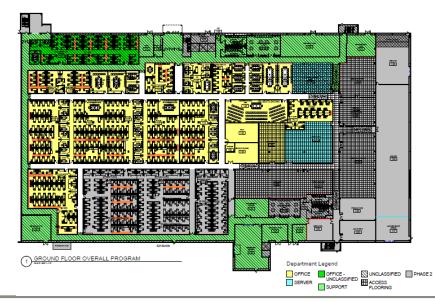

STATUS/CHALLENGES/WAY AHEAD

Status:

Actual

Pre-Solicitation Notice issued on 5 Feb 2019

Design of B9201 interior renovation and up-fit for aircraft Program Office (approx. 60,000 sqft) to include administrative space







Scheduled Key Action EEB 2019 Ready to Advertise (BTA)

FEB 2019	Ready to Advertise (RTA)	
APR 2019	Advertise	
JUL 2019	Award	

OKLAHOMA CITY VA MEDICAL CENTER

PROJECT INFORMATION

- **Project Title and Location:** FY17 Upgrade Interior Finishes
- Project Number/P2#: PN/ 464020
- Description / Scope: Design and construct interior upgrades to Ground and 1st Floors
- PA: \$2-4M
- Acquisition Strategy: DB, SDVOB MATOC
- Estimated Construction Completion (Physical Comp): May 2020
- PM: CPT Garrett D. Anderson



STATUS/CHALLENGES/PM ASSESSMENT

MILESTONES

Scheduled	Key Action	Actual
FEB / MAR 2019	Advertise	
MAY 2019	Award	

<u>Status</u>:

- ➢Package is RTA
- Scope is to design and construct interior renovations inside the Oklahoma City Veterans Medical Center







138TH FIGHTER WING ANG: FUEL STORAGE COMPLEX

PROJECT INFORMATION

- Project Title and Location: FY20 Fuel Storage Complex
 Project Number/P2#: PN/ 471097
- Description / Scope: Design and construct Fuel Storage Complex
- KTR: Omaha District (Designer)
- PA: \$12-18M
- Contract Amount: TBD
- Acquisition Strategy: DBB
- Estimated Construction Completion (Physical Comp): TBD
- PM: CPT Garrett D. Anderson

	MILESTONES	
Scheduled	Key Action	Actual
OCT 2019	Ready to Advertise (RTA)	
DEC 2019	Advertise	
MAR 2020	Award	



STATUS/CHALLENGES/PM ASSESSMENT

<u>Status</u>:

- Design underway
- Construct 2 each 2,500 BL welded steel above-ground fuel storage tanks complete with fixed cone-up welded steel roofs, internal full contact floating pans, stairs, railings, and other necessary appurtenances. Two covered commercial truck unloading stands and two covered refueler loading stands. Vehicle Fueling Station consisting of 8,000 gallons of diesel storage with two dispensing nozzles, 8,000 gallons of Motor Gas (MOGAS) storage with two dispensing nozzles, equipment.







16

PANTEX

PROJECT INFORMATION

- Project Title and Location: High Explosive Science & Engineering Facility (HES&E), PANTEX
- Description / Scope: Design a complex to consolidate 15 facilities into one to include HE Materials Lab, Tech Development & Deployment Lab, Admin & Office Area, and HE Staging Bunker
- **PA:** \$80-90M
- Designer: Burns and McDonnell
- Acquisition Strategy: Firm Fixed Price (DBB)
- Estimated Construction Completion (Physical Comp): 2024
- PM: Ruben Del Rio



STATUS/CHALLENGES/WAY AHEAD

MILESTONES

Scheduled	Key Action	Actual
JUL 2018	Ready to Advertise (RTA)	
JAN 2020	Advertise	
OCT 2020	Award	

Status:

- Construct a complex to consolidate 15 facilities into one to include High Explosive Materials Lab, Tech Development & Deployment Lab, Admin & Office Area, and High Explosive Staging Bunker
- Project advertisement pending Congressional budget approval







18 Questions 1 US Army Corps of Engineers ® U.S.ARMY
